

AFL
AFLO
AI FASHION LAB
TRY WITHOUT TRYING
FASHION
PRESENTATION



TABLE OF CONTENTS

1 Client details
2 Market Landscape
3 Client and Market
Problem Tree
4 AI Fashion Lab Solution
5 Content deliverables
6 Planning deliverables
7 Execution deliverables
Monitoring and control
8 COMPLETION
9 Deliverable

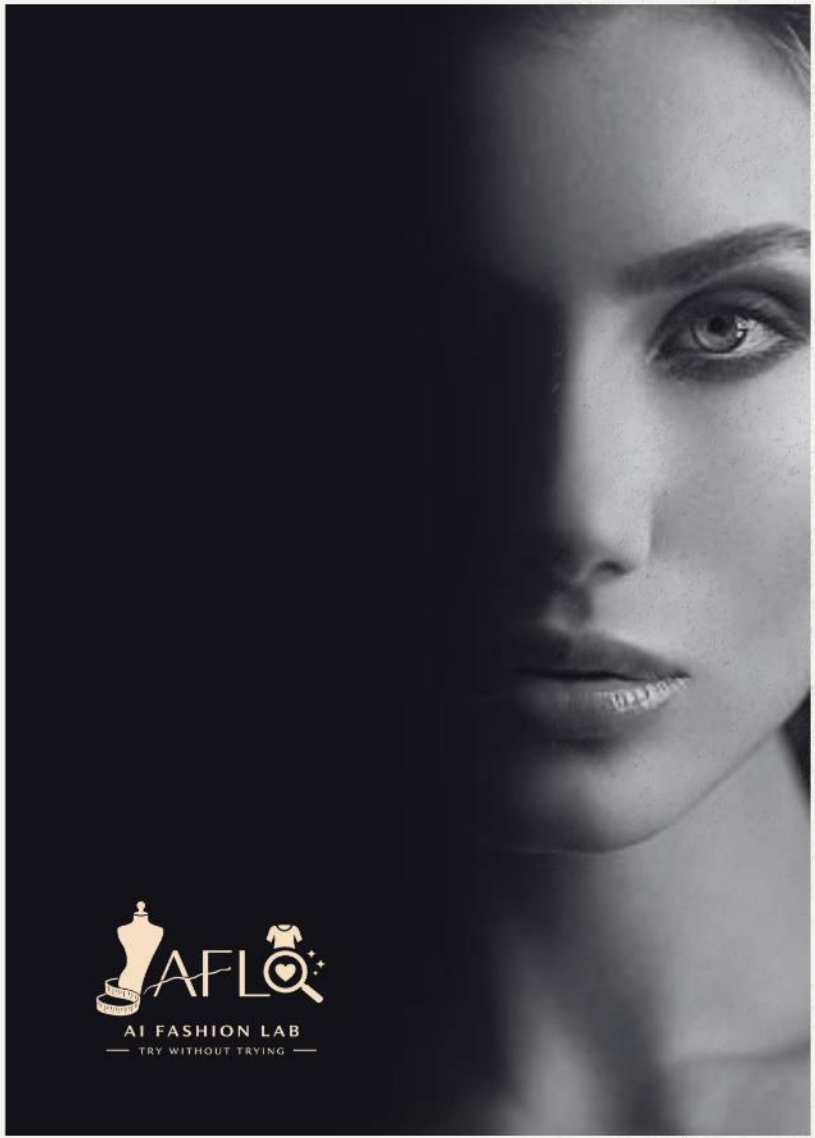

WELCOME

AI Fashion Lab

Where fashion meets artificial intelligence

AI Fashion Lab is an AI-powered platform for online luxury brands, helping them present products more clearly and build customer confidence before purchase.

A digital fashion tool that allows premium brands to turn product data into engaging, trustworthy shopping experiences.

.

AFLO
AI FASHION LAB
TRY WITHOUT TRYING

MARKET LANDSCAPE

Digital Luxury Fashion for Emerging Brands



Industry

Luxury and premium ready-to-wear fashion
Tops, coats, trousers, and everyday luxury items

Sales Channel

Mostly online
E-commerce and digital marketing
Few or no physical stores

Competitive pressure

Competing with established luxury houses
Lower brand recognition
Fewer financial and technical resources

AFLO
AI FASHION LAB
TRY WITHOUT TRYING

CLIENT & MARKET

The Client

Emerging Luxury Fashion Brands

- Small and growing premium fashion startups
- Sell mainly through their own websites and social media
- Limited marketing, IT, and operational resources
- Focus on high-quality ready-to-wear items (tops, coats, trousers)

The Market

Online Luxury Fashion

- Customers *expect high-end visual presetion online*
- Buying decisions are based on images, fit, and *brand brand trust*
- No physical stores for many emerging brands
- Strong competition from established luxury houses

Emerging luxury brands must compete *online* by building trust, visual appeal, and customer confidence *without the support of physical retail* or long brand histories.

AFLO
AI FASHION LAB
TRY WITHOUT TRYING

PROBLEM TREE

Why customers hesitate to buy fashion online

High Return Rates

Wrong size or style leads to product returns



Low Conversion Rates

Customers abandon their carts



Weak Brand Trust

Bad experiences reduce loyalty



Lack of confidence when buying fashion online

Customers are unsure about fit, look, and style before purchasing.



No Try-On Experience

Customers cannot see how clothes look on them



Sizing Uncertainty

Sizes differ by brand, cut, and fabric



AI FASHION LAB
TRY WITHOUT TRYING

SOLUTION — AI FASHION LAB PLATFORM

01



AI Virtual Try-On

- Upload a photo or outfit
- See how garments look on a character
- Create realistic visual concepts

02



Smart Size & Fit

- Enter basic body measurements
- Get accurate size suggestions
- Improve realism and reduce mistakes

03



Style & Character Matching

- Upload Pinterest or reference images
- Match costumes to style and character
- Explore different creative directions

Together, these modules turn costume ideas into clear, AI-powered visual concepts before production begins.

PLANING DELIVERABLES

From Vision to Execution:
Planning the 10-Week MVP

AFLQ
AI FASHION LAB
TRY WITHOUT TRYING



AFLO
AI FASHION LAB
TRY WITHOUT TRYING

Planning

SMART OBJECTIVES

- **Specific:** Launch a functional AI Virtual Try-On MVP.
- **Measurable:** Target 15% increase in purchase intent.
- **Achievable:** Pilot with 1-2 fashion brand partners.
- **Relevant:** Address sizing uncertainty & high return rates.
- **Time-bound:** 10-week fixed delivery schedule.

SCOPE MANAGEMENT

IN-SCOPE

- AI Generation Engine
- Size Recommendation AI
- Pinterest Integration
- Partner Dashboard

OUT-OF-SCOPE

- Physical Store Kiosks
- 3D Body Scanning
- Logistics Fulfillment

Constrains

- **Time: Fixed deadline for marketing launch**
- **Cost: €1.000.000 all inclusive budget cap**
- **Quality: Luxury-tier image generation standards**

Funding Cap
€1.000.000

Forcasted Cap
€823.400

👉 **Seeking Sponsor Approval for Execution Phase.**

AFLO
AI FASHION LAB
TRY WITHOUT TRYING

10-Week Roadmap

Discovery & Requirements

01 — M1

Kickoff, team alignment & requirement finalization

Project Kickoff

Technical Build & AI Training

02 — M2

UI/UX Prototypes & data governance protocols

Design Freeze

03

Backend Infra setup & API structure definition

04 — M3

Platform Core: Image processing live

Core Alpha

06 — M4

E2E Try-On Integration: First demo.

Go/No-Go Check

07

Brand Dashboard & Pinterest connection.

08 — M5

MVP Feature Complete: QA

Feature Freeze

09 — M6

Beta launch with Pilot Brand partners.

Beta Release

QA & Launch

05

AI Training Phase: Diffusion fine-tuning

10 — M7

Grand Launch & Ops Handover

Market Ready

AFLO
AI FASHION LAB
TRY WITHOUT TRYING

Success & Governance

Success Metrics (KPIs)

+10-15%
Purchase Intent

>95%
Try-On Success Rate

4.8/5
User UX Rating

-30%
Return Rate

Success is evaluated via delivery, quality, business impact, and operational readiness

Project Sponsor (Executive)
High-level decisions: Scope Pivot, Budget Release.

Project Manager
Operational decisions: controls schedule, risk, stakeholder communications

Technical Leads (AI/BE/UX)
Technical decisions: architecture, model selection and UI/UX flows

Reporting Cadence: Weekly Steering Updates + W5/6 "Go/No-Go" MVP checkpoint

EXECUTION DELIVERABLES

AI Virtual Try-On for Luxury Startups
Methodology · WBS · Precedence/CP · Gantt · MVPs + Sprints

AFLO
AI FASHION LAB
TRY WITHOUT TRYING



AFLO
AI FASHION LAB
TRY WITHOUT TRYING

Methodology

Hybrid (Waterfall + Agile)

We chose a Hybrid methodology because this project combines strict luxury-brand constraints with AI development.

WATERFALL (Structured)

Planning & Scope Lock
Define objectives, success metrics, scope (in/out), deliverables, milestones, and constraints for a 10-week project.

Infrastructure / Hardware Provisioning
Provision cloud GPUs, testing devices/edge hardware, and storage/backup to support AI training and platform reliability.

Governance & Documentation
Set roles (sponsor, PM, team), approval gates, reporting rhythm, and decision rules to stay aligned with luxury brand requirements.

Cost Baseline & Control
Build cost estimate + weekly cost baseline, define reserve usage rules, and monitor variance to remain within budget.

AGILE (Iterative)

Virtual Try-On Module
Iterate on model quality (fit realism, garment alignment), UX feedback loops, and performance tuning.

Smart Size Recommender
Develop measurement form + size logic per brand, test accuracy, reduce sizing uncertainty to lower returns.

Pinterest Style Matching
Build style analyzer + recommendation engine, test similarity quality, and simplify integration to reduce risk.


Incremental MVP Delivery
Deliver MVPs in sprints (Try-On → Size → Pinterest → Brand tools), validate with users/brands, then improve continuously.

Agile-at-the-edge | 10 weeks | ~€1M budget

AFL
AI FASHION LAB
TRY WITHOUT TRYING

WBS
Work breakdown Structure

Software Development

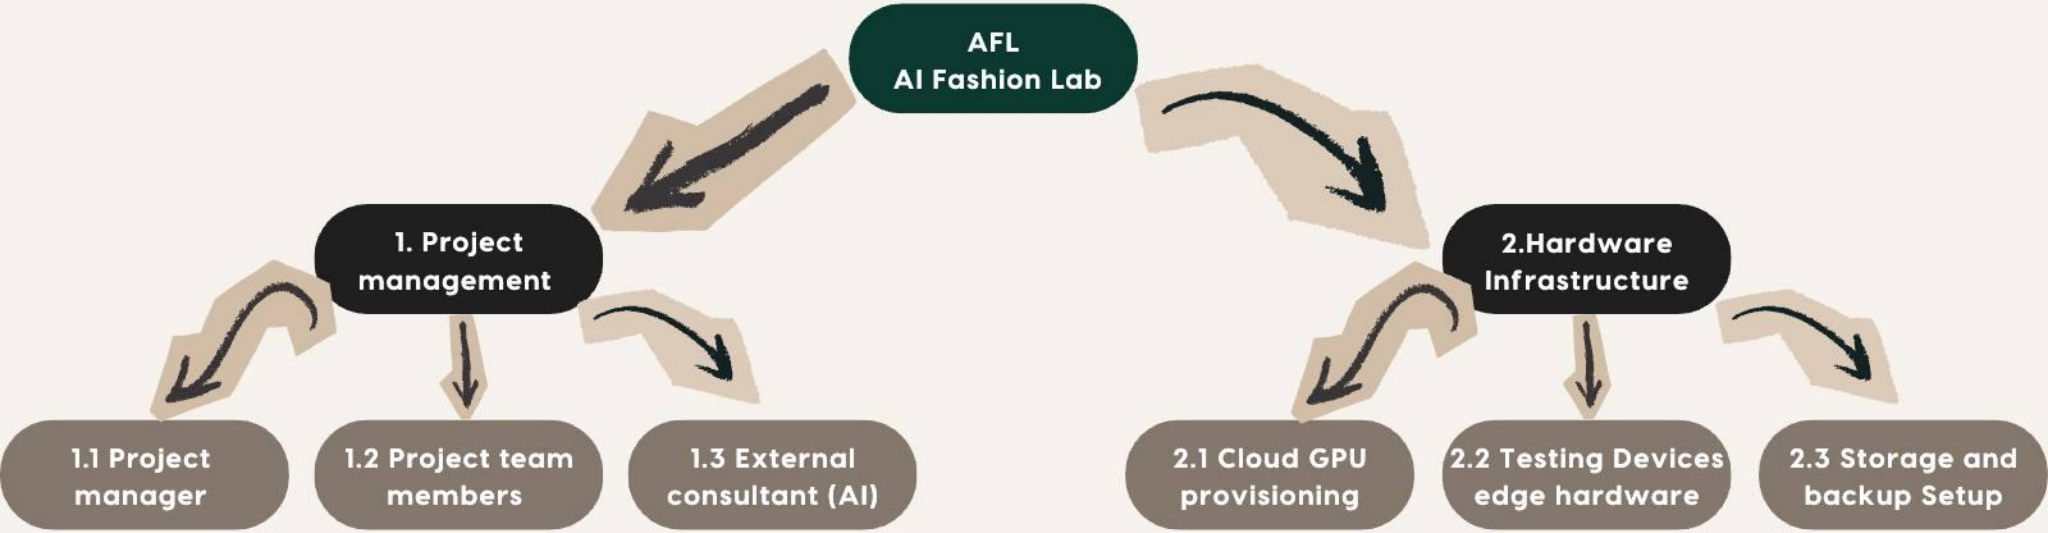

AFL
AI FASHION LAB
TRY WITHOUT TRYING

WBS
Part 2

AFL
AI Fashion Lab

Software Development

3.1 Virtual Try- On Engine
- 3.1.1 Image pipeline
- 3.1.2 Try-on model integration
- 3.1.3 Output rendering & quality checks

3.2 Smart Size Recommender
- 3.2.1 Measurement form + size mapping logic
- 3.2.2 Size recommendation module integration
- 3.2.3 Validation & calibration

3.3 Pinterest Style Analyser
- 3.3.1 Pinterest linking / inspiration upload
- 3.3.2 Style similarity logic
- 3.3.3 Product recommendation output

3.4 Web platfrom and mobile UX
- 3.4.1 Customer interface
- 3.4.2 Brand dashboard
- 3.4.3 Backend services
- 3.4.4 GDPR & security features


3.5 Integration and deployment
- 3.5.1 Catalog ingestion
- 3.5.2 End-to-end integration of modules
- 3.5.3 Deployment pipeline + monitoring instrumentation

AFL
AI FASHION LAB
TRY WITHOUT TRYING

WBS
Part 3



Precedence Diagram + Critical Path

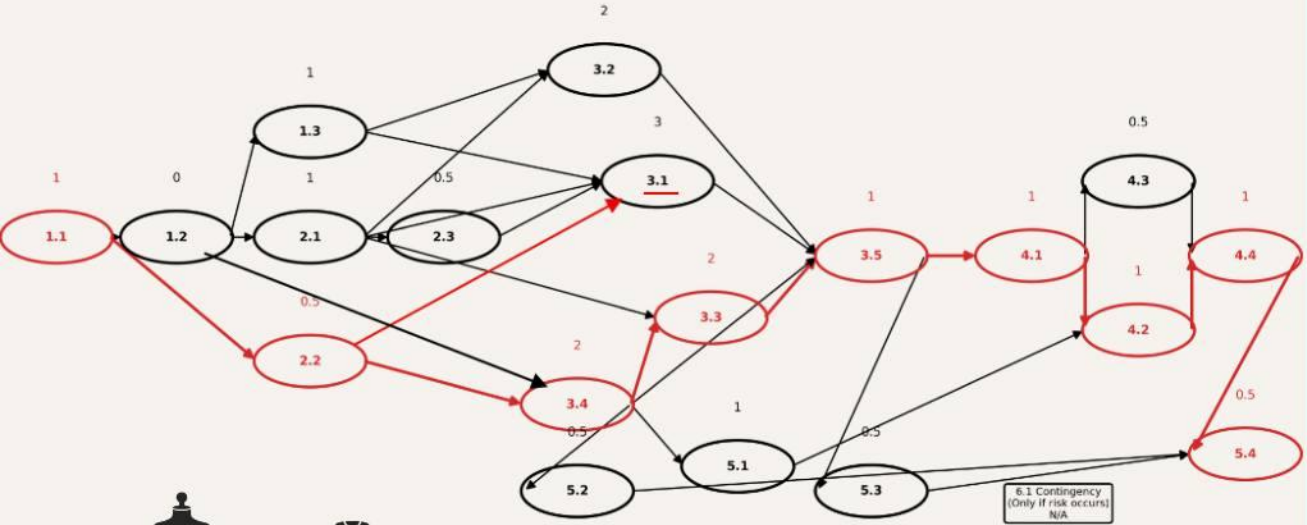

AFLO
AI FASHION LAB
TRY WITHOUT TRYING

- Oval = Task ID
  Number above the oval = Duration (weeks)
  Arrow (→) = Dependency / Predecessor relationship (Finish-to-Start)
- The task at the start of the arrow must be completed before the next task can begin.
- Red ovals + red arrows = Critical Path
  This is the longest chain of dependent tasks. Any delay on a red task delays the entire project.
- Black ovals/arrows = Non-critical tasks
  These tasks have float/slack (they can shift slightly without delaying the end date), as long as they stay within their allowed slack.
- Parallel branches = Work that can run at the same time
- When multiple arrows leave one task, it means several tasks can start in parallel after that predecessor is done.
- 6.1 Contingency = Not planned work: it is used only if a risk happens and contingency budget/time is needed.

Activity Table


snapshot

Task ID	Task description (lowest level)	Duration (weeks)	Predecessor(s)
1.1	Project Manager (kickoff/governance)	1.0	–
1.2	Project Team Members (planning & coordinatio	1.0	1.1
1.3	External Consultants (AI feasibility/advice)	1.0	1.2
2.1	AI training servers (Cloud GPU provisioning)	1.0	1.2
2.2	Testing devices & edge hardware setup	1.0	1.2
2.3	Storage & backup systems setup	0.5	2.1
3.1	Virtual Try-On Engine	3.0	1.3, 2.1, 2.3
3.2	Smart Size Recommender	2.0	1.3, 2.1
3.3	Pinterest Style Analyzer & Recommendations	2.0	2.1, 3.4
3.4	Web Platform & Mobile UX	3.0	1.2, 2.2
3.5	Integration & Deployment	1.0	3.1, 3.2, 3.3, 3.4

AFLO
AI FASHION LAB
TRY WITHOUT TRYING

Gantt chart

Task ID	Task Name	Duration (wks)	Start (wk)	End (wk)	Predecessor(s)
1. Project Management					
1.1	Project Manager	1	1	2	–
1.2	Project Team Members (parallel with 1.1)	0	1	1	1.1(SS)
1.3	External Consultants focus on AI	1	2	3	1.2(FS)
2. Hardware & Infrastructure					
2.1	AI training servers (Cloud GPU provisioning)	1	2	3	1.2 (FS)
2.2	Testing devices & edge hardware setup	0,5	2	2,5	1.2(FS)
2.3	Storage & backup systems setup	0,5	3	3,5	2.1(FS)
3. Software Development					
3.1	Virtual Try-On Engine	3	3,5	6,5	1.3(FS), 2.1(FS), 2.3(FS)
3.2	Smart Size Recommender	2	3	5	1.3(FS), 2.1(FS)
3.3	Pinterest Style Analyzer	2	4,5	6,5	3.4(FS), 2.1(FS)
3.4	Web Platfrom and Mobile UX	2	2,5	4,5	2.2(FS),1.2(FS)
3.5	Integration & Deployment	1	6,5	7,5	3.1(FS), 3.2(FS), 3.3(FS), 3.4(FS)
4. Testing & QA					
4.1	System integration testing	1	7,5	8,5	3.5(FS)
4.2	User acceptance testing (pilot brands)	1	8,5	9,5	4.1(FS),5.1(FS)
4.3	Performance & stability testing	0,5	8,5	9	4.1(FS)
4.4	Bug fixes & optimization	1	9	10	4.2(FS), 4.3(FS)
5. Training & Support					
5.1	Brand onboarding + documentation	1	4,5	5,5	3.4(FS)
5.2	Customer support setup	0,5	4,5	5	3.4(FS)
5.3	AI maintenance & monitoring plan	0,5	7,5	8	3.5(FS)
5.4	Operational support & hosting readiness	0,5	9,5	10	4.4(FS), 5.2(FS), 5.3(FS)
Milestones					
M1	Kickoff & governance approved		2	2	End of 1.1
M2	MVP Demo (Platform + core flows)		4,5	4,5	End of 3.4
M3	Integration complete		7,5	7,5	End of 3.5
M4	Beta/UAT sign-off		10,5	10,5	End of 4.4
M5	Go-live / Operational readiness		11	11	End of 5.4

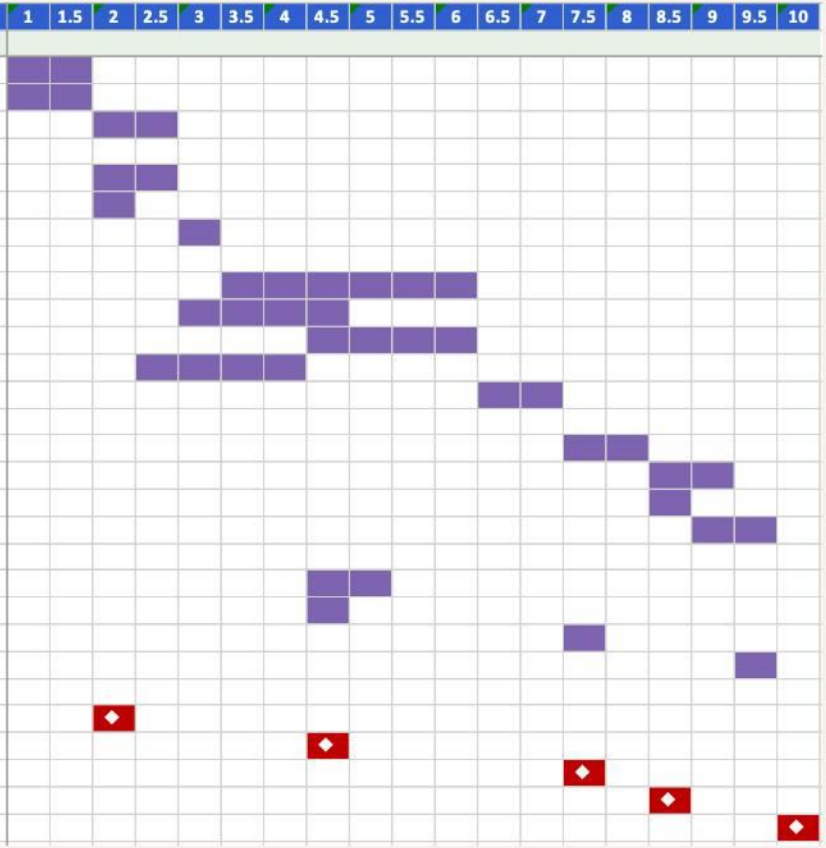

AFLO
AI FASHION LAB
TRY WITHOUT TRYING

Milestones
From the Gantt chart

Milestones mark the key decision and validation points that confirm the project's readiness to move to the next phase, from kickoff to go-live.

M1 : KICKOFF AND GOVERNANCE APPROVED

THE PROJECT START WITH A SCOPE, DEFINE ROLES AND GOVERNANCE VALIDATED

M2: MVP DEMO

MINIMUM VIABLE PRODUCT TO GO TO A FUNCTIONAL DEMO FOR SPECIFICALLY THE PLATFORM AND MAIN USER JOURNEY

M3: INTEGRATION COMPLETE

EVERY CORE MODULES ARE SUCCESSFULLY INTEGRATED IN ONE SYSTEM

M4: BETA/UAT SIGN OFF

HAVE VALIDATION POINT WHERE BRAND CONFIRMING USABILITY AND UTILIZATION OF THE MODULES

M5: GO-LIVE

AFLO
AI FASHION LAB
TRY WITHOUT TRYING

Sprint

SPRINTS ARE SHORT, TIME-BOXED AGILE ITERATIONS USED TO DEVELOP, TEST, AND VALIDATE INCREMENTAL FEATURES OF THE AI VIRTUAL TRY-ON PLATFORM, ALLOWING CONTINUOUS FEEDBACK AND REFINEMENT OF CORE MODULES SUCH AS TRY-ON, SIZING, AND STYLE MATCHING.

SPRINT 1 (WEEK 2): PLATFORM FOUNDATION

GOAL: THE AIM IS TO CREATE A WORKING UPLOAD PIPELINE, STORAGE AND BASIC UI SKELETON.

BACKLOG ITEMS: UPLOAD A PHOTO, AND THEN I RECEIVE A TRY-ON RESULT.

SPRINT 2 (WEEK 3) – MVP1: BASIC TRY-ON DEMO

GOAL: TO PRODUCE FIRST TRY-ON OUTPUT

BACKLOG ITEMS: TRY A V1 INTEGRATION WITH SEGMENTATION AND POSE PIPELINE

SPRINT 3 (WEEK 4) – MVP2: SIZE RECOMMENDER BUILD

GOAL: TO HAVE THE BEST SIZE RECOMMENDATION FEATURE

BACKLOG ITEMS: WHEN A USER ENTERS HIS/HER DATA ABOUT HIS BODY TYPES AND SIZE, NEED TO FEEL COMFORTABLE AND A GOOD SYSTEM THAT RECOMMEND HIS/HER SIZE.

SPRINT 4 (WEEK 5) – INTEGRATION & QUALITY HARDENING

GOAL: TO CONNECT MODULES AND MAKE THE EXPERIENCE RELIABLE ENOUGH FOR CUSTOMER (COMPANIES) AND END-CUSTOMERS

BACKLOG ITEMS: INTO THE PRODUCT SELECTION (LUXURY-BRAND) INTEGRATE SIZE RECOMMENDER.THIS CAN GET US AN ONLINE TRY-ON RESULT

SPRINT 5 (WEEK 6) – MVP3: PINTEREST STYLE ANALYZER V1

GOAL: WE ARE PUTTING THIS INNOVATION TO BRING INSPIRATION PINTEREST GALLERY AND GET RECOMMENDATIONS FROM LUXURY PARTNER.

BACKLOG ITEMS: TO IMPORT LINK OF PINTEREST INSPIRATIONS SO THE GUIDING SYSTEM CAN UNDERSTAND YOUR STYLE.


AFLO
AI FASHION LAB
TRY WITHOUT TRYING

MVPs

minimum viable products



UPLOAD PHOTO TO VIRTUAL TRY-ON




DATA MEASUREMENT TO GET SIZE RECOMMENDATION



PINTEREST CATALOG INSPIRATION WITH YOUR STYLE MATCHING

AFLO
AI FASHION LAB
TRY WITHOUT TRYING

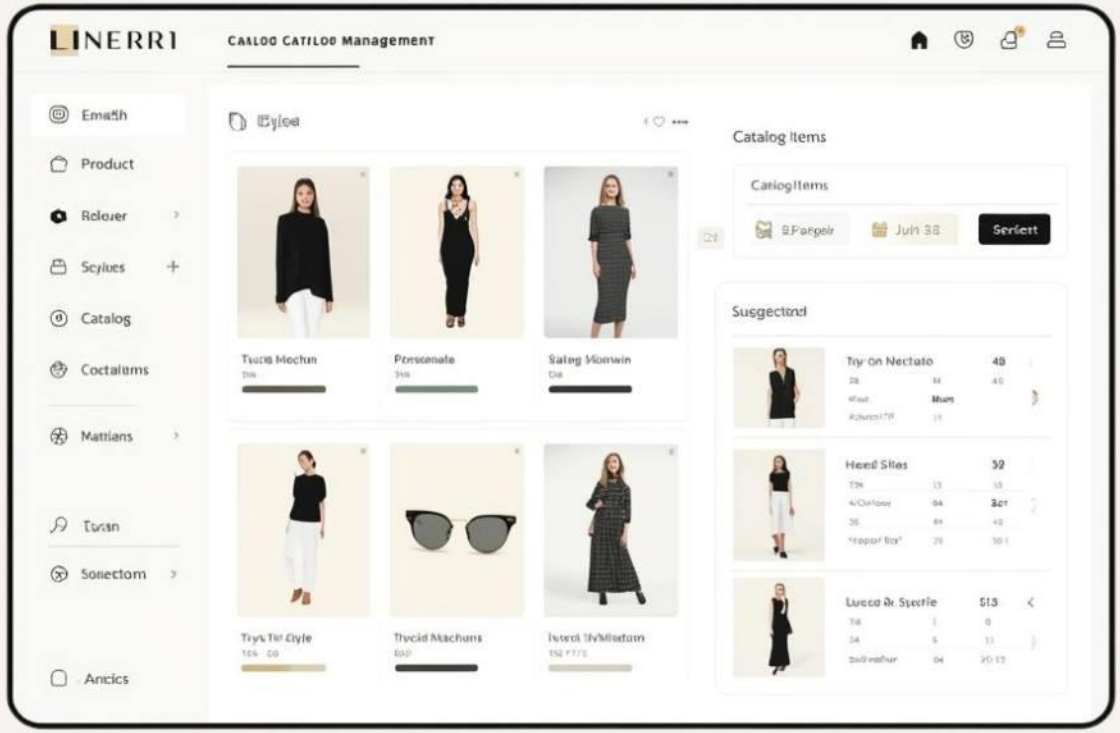

PUT THOSE FUNCTIONALITIES ON THE BRAND DASHBOARD AND THAT CAN MATCH THE CATALOG SUGGESTION.

MONITORING & CONTROL

Ensuring alignment with scope, cost, schedule, and quality

AFLO
AI FASHION LAB
TRY WITHOUT TRYING



AI FASHION LAB
TRY WITHOUT TRYING

Monitoring & Control

Continuous control is critical due to:

- **Fixed 10-week schedule**
- **€1M budget cap**

High technical uncertainty (AI models)

Control activities focus on three core areas:

- **Cost management**
- **Risk management**
- **Stakeholder management**

Monitoring & Control is critical so the project remains aligned with approved:




AFLO
AI FASHION LAB
TRY WITHOUT TRYING

Risk Management & Mitigation Strategy

Budget at Completion (BAC): €823,400

Costs structured by WBS categories

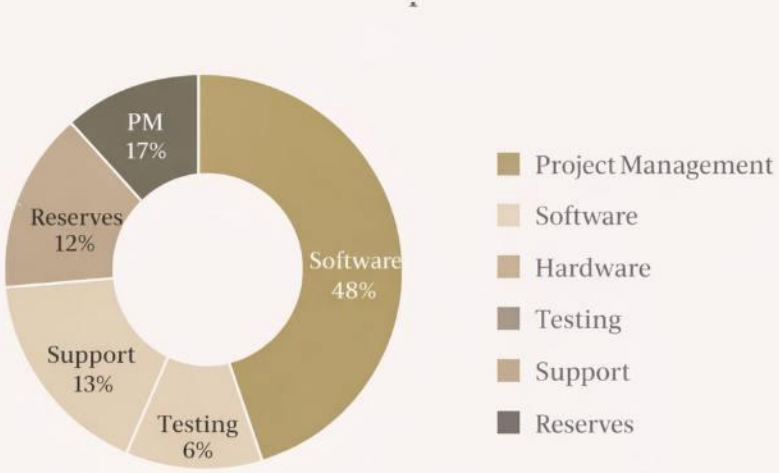

Weekly cost tracking using EVM-lite




Corrective action if CPI < 0.9

Contingency reserve (~12%) for AI-related risks

AFLO
AI FASHION LAB
TRY WITHOUT TRYING

Cost Management & Financial Control

Risk Matrix

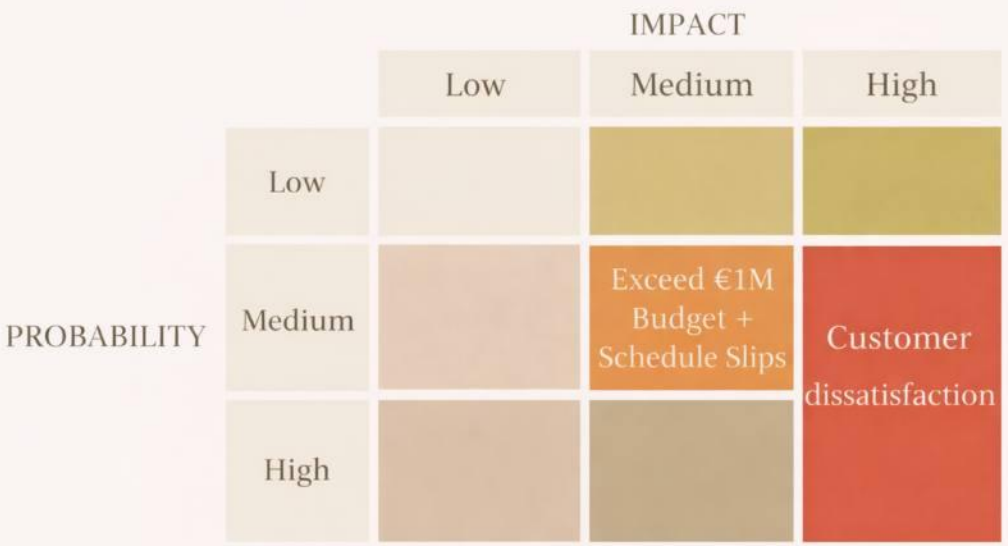

1) AI OUTPUT QUALITY BELOW LUXURY STANDARDS

2) LOW-QUALITY PRODUCT IMAGES OR METADATA FROM PARTNER BRANDS

3) GDPR & PRIVACY RISKS RELATED TO CUSTOMER PHOTO


4) CLOUD INFRASTRUCTURE COST VOLATILITY

Weekly risk review & escalation

AI FASHION LAB
TRY WITHOUT TRYING

Stakeholder Monitoring & Alignment

Stakeholder Map

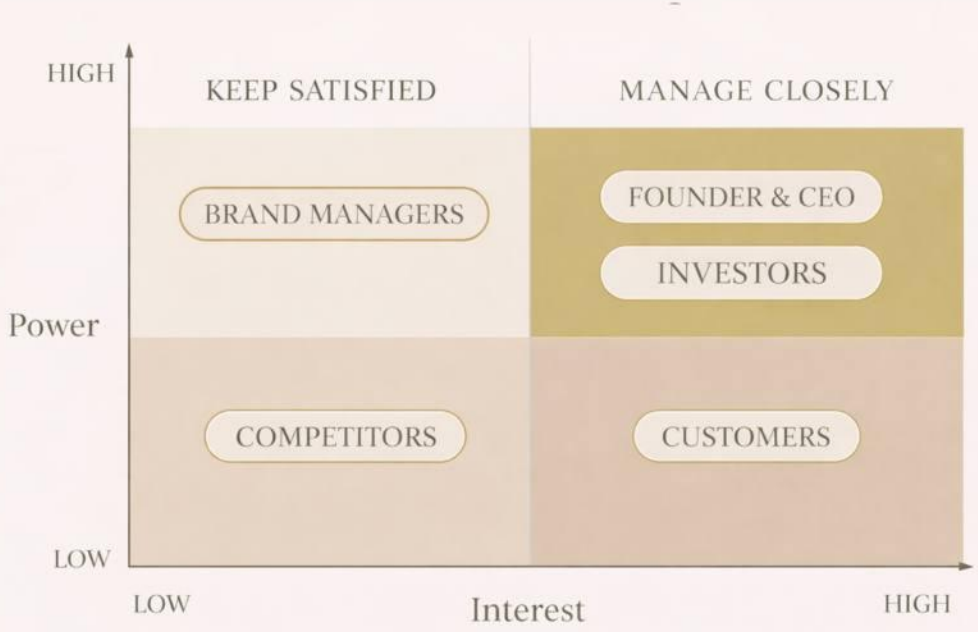

Sponsor: weekly steering updates

Partner brands: onboarding & quality checkpoints

End customers: UX feedback & beta testing

Internal teams: sprint reviews & demos

Objective: alignment, trust, and adoption

COMPLETION: BENEFITS REALIZATION

Managing Adoption and Measuring Value After Launch

AFLQ
AI FASHION LAB
TRY WITHOUT TRYING



AFLO
AI FASHION LAB
TRY WITHOUT TRYING

Benefits Realization Map

Measuring success through practical outcomes for luxury startups

BENEFIT	KPI	HOW MEASURED	OWNER	TARGET TIMING
Conversion Uplift	Add-to-cart rate	Web Analytics / A/B Test	E-commerce Lead	+4–8 weeks post-launch
Reduce Returns	Size-related return %	Returns Dashboard	Brand Ops Lead	1–3 months post-launch
Trust Increase	CSAT, NPS score	Post-Try-On Survey	Product/UX Lead	4 weeks post-launch
Reduce Friction	Drop-off in flow %	Funnel Analytics	UX Lead	Weekly post-launch
Support Efficiency	Tickets per 1k orders	Helpdesk Analytics	Support Lead	Month 1–2 post-launch

Pilot Success Targets

Conversion: +5-10% | Returns: -10-20% | CSAT: 4.2/5.0+

Proves value creation, not just technical outputs

AFLO
AI FASHION LAB
TRY WITHOUT TRYING

Tracking & Governance

WE DON'T JUST LAUNCH, WE ADAPT

Baseline Snapshot (Pre-Launch)

Conversion Rate	**X%**
Return Rate	**Y%**
Size-related Share	**Z%**

Weekly (Month 1)

Conversion funnel performance, try-on completion rates, and CSAT scores.

Monthly

Size-related return rates and estimated operational cost savings.

Quarterly

Long-term NPS trends and early customer retention/loyalty signals.

Post-Launch Milestones

W+2: Try-on completion signals.
W+4: Conversion uplift evidence.
M2-3: Final returns impact analysis.



Governance Framework

01 Regular Updates

Leads from Product, Ops, and Support check their numbers and share monthly progress reports.

02 Management Review

The Project Sponsor checks if we are hitting our goals. If not, we decide how to adjust the plan.

03 Fixing Issues

If the results are lower than expected, we take immediate action:

POSSIBLE CHANGES

- Make UI simpler
- Better instructions
- Retrain AI models
- Speed up the app

AFLO
AI FASHION LAB
TRY WITHOUT TRYING

WHO IS AFFECTED BY THE CHANGE

Key Stakeholder Groups

LUXURY BRAND PARTNERS



PROVIDE PRODUCT DATA, IMAGES, AND APPROVE AI OUTPUTS

CUSTOMERS (BUYERS)



UPLOAD PHOTOS, GET SIZE ADVICE, VIEW AI TRY-ONS

INTERNAL TEAMS



SUPPORT, DEVOPS, AND AI TEAMS RUNNING THE PLATFORM

LEADERSHIP (CEO / SPONSOR)



OVERSEES SCOPE, PERFORMANCE, AND DIRECTION

AFLO
AI FASHION LAB
TRY WITHOUT TRYING

What Changes for Brand Partners

Luxury Brand Partners

What changes

- Higher-quality product images, size tables, and metadata
- New onboarding and catalogue submission process

Main concerns

- Brand image may be affected
- Extra work preparing assets
- Control over product images and IP

Main concerns

- Fear that AI images may harm luxury brand image
- Extra work preparing assets
- Control over product images and IP

How it's managed

- Brand quality rules and approval of AI outputs
- Templates, checklists, and onboarding support
- Small pilot with limited SKUs before scaling
- Small pilot with limited SKUs before scaling

AI FASHION LAB
TRY WITHOUT TRYING

CHANGE MANAGEMENT

ADKAR Model for Emerging Luxury Fashion Startups

A
Awareness

Explain the need for AI solutions in online luxury fashion



D
Desire

Motivate luxury brands to be open to adopting AI



K
Knowledge

Educate startups on how AI can enhance their online stores



A
Ability

Provide tools and support for using AI effectively



R
Reinforcement

Encourage long-term engagement and improvement



Guide luxury startups on how to embrace AI, from awareness to sustained use.

Conclusion & Next Steps

WHAT WE DELIVERED

- A STRUCTURED PLAN FOR AFL, AN AI SERVICE FOR LUXURY STARTUPS: TRY-ON + SIZE + STYLE MATCH
- CLEAR EXECUTION FRAMEWORK: WBS → ACTIVITY TABLE → PRECEDENCE & CRITICAL PATH → 10-WEEK GANTT
- FINANCIAL CONTROL: COST ESTIMATE + COST BASELINE + RESERVES (≤ €1M)



AFL
AI FASHION LAB
TRY WITHOUT TRYING

WHY IT MATTERS

- BUILDS TRUST FOR NEW LUXURY BRANDS
- REDUCES SIZE UNCERTAINTY → LOWERS RETURNS
- INCREASES CONVERSION THROUGH CONFIDENT PURCHASE DECISIONS

NEXT STEPS AFTER GO-LIVE

- RUN BETA FEEDBACK LOOP AND IMPROVE MODEL QUALITY
- EXPAND BRAND INTEGRATIONS AND CATALOG COVERAGE
- TRACK KPIS (CONVERSION UPLIFT, RETURN RATE REDUCTION, NPS/CSAT)



THANK YOU



AI FASHION LAB

TRY WITHOUT TRYING
